

SIX NINE CONSTRUCTION (PVT) LTD

Grade-1 Complete Construction Project Brief & Pack

Client contract value: USD 223,647.79 | 7.7% protected margin | 12-week programme

Project Reference ID: SNC-FULL-QT-2026-001

Prepared For	Full Documentation Test Client
Project Name	Industrial Warehouse Extension
Contract Value	\$223,647.79
Project Duration	12 Weeks / 60 Workdays
Status	Grade-1 Construction & Estimating Blueprint

Table of Contents

Section 1: Executive Summary & Project brief	Page 2
Section 2: Assumptions, Exclusions & Clarifications	Page 3
Section 3: Quotation Financial Summary	Page 4
Section 4: BOQ Section Totals Analysis	Page 5
Section 5: Detailed Bill of Quantities (BOQ) Ledger	Page 6
Section 6: Margin Protection Control Sheet	Page 7
Section 7: Required Materials & Price Targets	Page 8
Section 8: Supplier RFQ & Verification Controls	Page 10
Section 9: Material Margin Controls by Package	Page 11
Section 10: Construction Operations & Controls	Page 12
Section 11: Programme Sensitivity - Best/Expected/Delay Case	Page 13
Section 12: Monthly Target Revenue & Spend Outlay	Page 16
Section 13: Monthly Cash Flow S-Curve	Page 17
Section 14: Weekly Execution Plan (Weeks 1 to 36)	Page 18
Section 15: Daily Execution Plan (Days 1 to 180)	Page 22
Section 16: Commercial Risk Register & Mitigation	Page 37
Section 17: Procurement & Supply Chain Strategy	Page 40
Section 18: Resource & Crew Requirements Plan	Page 41
Section 19: Health, Safety & QA/QC Checklists	Page 43
Section 20: Payment Milestones & Deliverables	Page 45

Executive Summary


Objective	Deliver Industrial Warehouse Extension for Full Documentation Test Client with controlled scope, phased procurement, weekly production targets, daily controls, and closeout documentation.
Assumed product	Scope as measured/allowed in the attached Bill of Quantities, priced from the 7-line Bill of Quantities attached to this pack.
Commercial result	Protected gross profit is \$17,250.90, equal to 7.7% margin. Total contract value is \$223,647.79.
Programme result	12 weeks from mobilisation to closeout, assuming approved drawings, clear site access, stable material supply, and no abnormal ground conditions.
Decision required	Client must approve final design, finishes schedule, provisional sums, authority route, payment milestones, and variation control before construction starts.

Core Assumptions and Exclusions

Assumptions	Normal soil bearing, no rock blasting, no contaminated material, no flood mitigation works beyond standard stormwater, uninterrupted client approvals, and imported finishes available within normal lead times.
Exclusions	Land purchase, professional design fees before construction appointment, finance charges, abnormal authority fees, borehole drilling, swimming pool, solar plant, generator, premium imported appliances beyond allowance, and client-initiated variations.
Quality class	Durable high-spec residential finish, not ultra-luxury. Finishes are controlled through allowances to protect the budget.
Contract control	Fixed-scope price with provisional sums and a controlled variation register. No margin changes without written authorization.
Currency	All values are USD values and should be revalidated against live supplier quotations before signature.

Quotation Financial Summary

Direct BOQ works	\$134,257.50	Trade packages and measured works
Preliminaries & General	\$9,500.00	Corporate mobilisation and site setups
Overheads	\$10,781.81	Head office resource allocation
Contingency	\$9,344.24	Held for measurable construction uncertainty
Protected profit	\$17,250.90	7.7% margin on client contract value
Quotation total	\$223,647.79	Client contract value

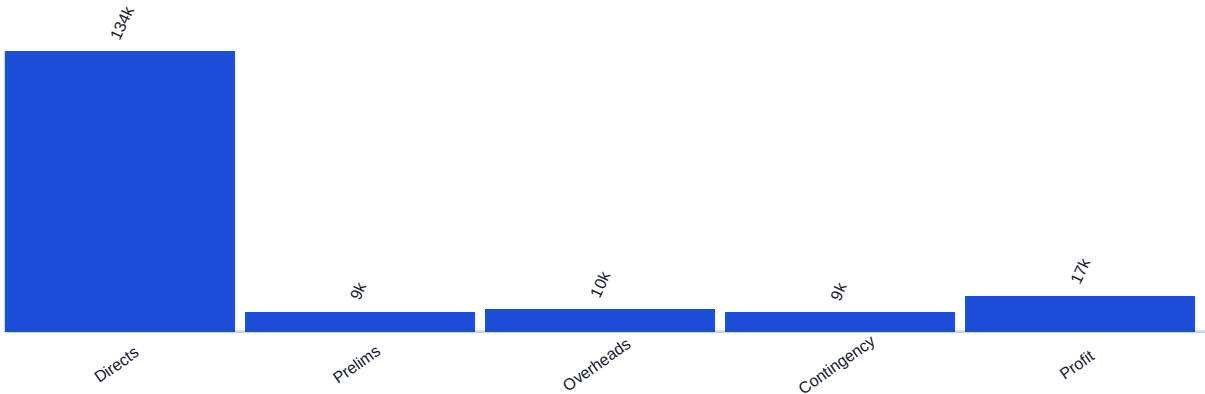

BOQ Section Totals Analysis

Preliminaries	\$9,500.00	4.2%
Roof sheeting and flashings	\$40,150.00	18.0%
Structural steel supply and installation	\$25,560.00	11.4%
Reinforced concrete foundations	\$22,260.00	10.0%
Electrical first fix and distribution	\$18,750.00	8.4%
Plumbing and drainage installation	\$14,200.00	6.3%
Bulk earthworks and cart-away	\$10,837.50	4.8%
Site establishment and setting out	\$2,500.00	1.1%
Protected Profit	\$17,250.90	7.7%

Detailed Bill of Quantities Ledger

0.01	Direct Works	Site establishment and setting out	item	1.00	\$2,500.00	\$2,500.00
0.02	Direct Works	Bulk earthworks and cart-away	m3	850.00	\$12.75	\$10,837.50
0.03	Direct Works	Reinforced concrete foundations	m3	120.00	\$185.50	\$22,260.00
0.04	Direct Works	Structural steel supply and installation	ton	18.00	\$1,420.00	\$25,560.00
0.05	Direct Works	Roof sheeting and flashings	m2	2,200.00	\$18.25	\$40,150.00
0.06	Direct Works	Electrical first fix and distribution	item	1.00	\$18,750.00	\$18,750.00
0.07	Direct Works	Plumbing and drainage installation	item	1.00	\$14,200.00	\$14,200.00

Margin Protection Control Sheet

Client Contract Value	\$223,647.79	This is the selling price ceiling agreed with the client.
Protected Gross Profit	\$17,250.90	This is company profit. It must be protected before any discretionary upgrade is accepted.
Maximum Internal Cost	\$206,396.89	All labour, materials, subcontractors, plant, and prelims must stay below this.
Direct Works Target	\$134,257.50	Measured BOQ delivery target after value engineering.
Construction Contingency	\$9,344.24	Used only for approved construction risk, not client upgrades.

Ruthless commercial rule: every requested upgrade, acceleration, rework, delay, scope clarification, or specification change must be priced before execution. Do not absorb client-driven costs inside contingency.

Highest-Value BOQ Line Items to Price-Lock First

Roof sheeting and flashings	m2	2,200.00	\$18.25	\$40,150.00	29.9%
Structural steel supply and installation	ton	18.00	\$1,420.00	\$25,560.00	19.0%
Reinforced concrete foundations	m3	120.00	\$185.50	\$22,260.00	16.6%
Electrical first fix and distribution	item	1.00	\$18,750.00	\$18,750.00	14.0%
Plumbing and drainage installation	item	1.00	\$14,200.00	\$14,200.00	10.6%
Bulk earthworks and cart-away	m3	850.00	\$12.75	\$10,837.50	8.1%
Site establishment and setting out	item	1.00	\$2,500.00	\$2,500.00	1.9%

Supplier RFQ and Price-Fetch Matrix

1. Supplier Master	Create approved supplier records with category, contacts, and tax registrations.	Prevents buying from unverified suppliers who can fail quality.
2. Three-Quote Rule	Capture preferred, backup and challenger quotes for every critical package.	Creates leverage and gives a replacement path if the first supplier fails.
3. Live Price Fetch	Pull prices from supplier portals/APIs; attach emailed PDFs to quote.	Avoids stale rates. Every price must have a timestamp and source.
4. Price Lock	Convert accepted supplier quote to purchase order before quote expiry.	Stops supplier escalation from silently eroding profit.

Material Margin Controls by Package

Concrete	Ready-mix concrete 25MPa	Verify delivery note volume matches slump test density before offloading.
Masonry	Cement Bags (50kg)	Store in watertight container; reconcile bags used daily against wall square meters.
Steel	Reinforcing rebar	No cutting list release without engineer-approved shop drawings.
Finishes	Porcelain tiles	Client upgrades are variations; select tile batches at once to avoid color mismatches.

What Else Makes This Work Operationally

Supplier Quote Register	Stores quote source, fetch date, expiry, and delivery cost.	You cannot prove why a rate was used or recover price movements.
Procurement Approval Workflow	Blocks purchase orders above budget or expired quotes.	Buying happens emotionally and margin disappears package by package.
Variation Order Workflow	Client upgrades or late decisions are signed before execution.	Free work accumulates and the profit margin becomes fiction.
Daily Cost Capture	Foreman captures labour hours, material usage, and blockers daily.	You cannot see which day started the loss.

Programme Sensitivity - Best / Expected / Delay Case

Best Case	11 Weeks / 55 Days	\$18,975.99	8.5%	Fast approvals, stable weather, zero rework.
Expected Case	12 Weeks / 60 Days	\$17,250.90	7.7%	Base quotation timeline. Normal lead times.
Delay Case	15 Weeks / 75 Days	\$12,075.63	5.4%	Late drawings, rain delays, unrecovered overhead burn.

Best/delay case profit figures are a +/-10%/30% sensitivity assumption applied to this quotation's real protected profit, not the output of a statistical simulation.

Schedule Driver Simulation Matrix

Site Conditions	Clean access, normal soil, no hidden lines.	Minor ground adjustments absorbed.	Rock or groundwater discovered.	Stop, photograph, and price variation before digging.
Weather	Dry conditions during earthworks and roofing.	Normal rain disruption within float.	Heavy storms flood trenches.	Weather diary, EOT notice, adjust sequencing.
Client Decisions	All selections made before week 1.	Decisions match decision schedule.	Late changes block orders.	Issue time and cost variation order. No free acceleration.


How the 12-Week Baseline Was Built

Mobilisation & design freeze	Weeks 1-1	Allows contract setup, permits, safety plans, and long-lead orders before site risk starts.
Groundworks and foundations	Weeks 2-3	Covers site clearance, bulk earthworks, foundation trenching, and rebar setups.
Substructure & shell walls	Weeks 4-4	Covers slabs pouring, gables masonry, columns casting, and wall plate scaffolding.
Roof and envelope dry-in	Weeks 5-5	Gets the building weather-tight so internal wet trades and cabinetry can begin safely.

Monthly Targets, Spend and Protected Profit

Month 1	Deliverables phase for Month 1	\$34,807.50	\$39,362.06	\$4,472.46
Month 2	Deliverables phase for Month 2	\$64,642.50	\$73,100.97	\$8,305.99
Month 3	Deliverables phase for Month 3	\$34,807.50	\$39,362.06	\$4,472.46

Monthly Cash Flow Curve

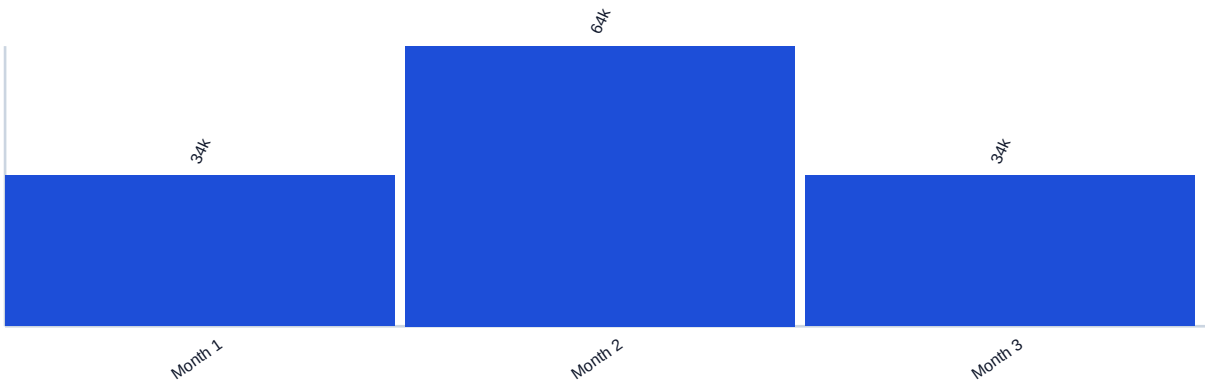

Weekly Execution Plan - Weeks 1 to 9

Week 1	Mobilisation / Site Setup	Mobilisation / Site Setup activities and RFI lockups for week 1.	Approved weekly report W1, inspection diary completed.
Week 2	Mobilisation / Site Setup	Mobilisation / Site Setup activities and RFI lockups for week 2.	Approved weekly report W2, inspection diary completed.
Week 3	Mobilisation / Site Setup	Mobilisation / Site Setup activities and RFI lockups for week 3.	Approved weekly report W3, inspection diary completed.
Week 4	Mobilisation / Site Setup	Mobilisation / Site Setup activities and RFI lockups for week 4.	Approved weekly report W4, inspection diary completed.
Week 5	Mobilisation / Site Setup	Mobilisation / Site Setup activities and RFI lockups for week 5.	Approved weekly report W5, inspection diary completed.
Week 6	Mobilisation / Site Setup	Mobilisation / Site Setup activities and RFI lockups for week 6.	Approved weekly report W6, inspection diary completed.
Week 7	Mobilisation / Site Setup	Mobilisation / Site Setup activities and RFI lockups for week 7.	Approved weekly report W7, inspection diary completed.
Week 8	Mobilisation / Site Setup	Mobilisation / Site Setup activities and RFI lockups for week 8.	Approved weekly report W8, inspection diary completed.
Week 9	Mobilisation / Site Setup	Mobilisation / Site Setup activities and RFI lockups for week 9.	Approved weekly report W9, inspection diary completed.

Weekly Execution Plan - Weeks 10 to 12

Week 10	Substructure Concrete	Substructure Concrete activities and RFI lockups for week 10.	Approved weekly report W10, inspection diary completed.
Week 11	Substructure Concrete	Substructure Concrete activities and RFI lockups for week 11.	Approved weekly report W11, inspection diary completed.
Week 12	Substructure Concrete	Substructure Concrete activities and RFI lockups for week 12.	Approved weekly report W12, inspection diary completed.

Daily Execution Plan - Days 1 to 12

1	1	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
2	1	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
3	1	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
4	1	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
5	1	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
6	2	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
7	2	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
8	2	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
9	2	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
10	2	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
11	3	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
12	3	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52

Daily Execution Plan - Days 13 to 24

13	3	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
14	3	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
15	3	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
16	4	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
17	4	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
18	4	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
19	4	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
20	4	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
21	5	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
22	5	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
23	5	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
24	5	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52

Daily Execution Plan - Days 25 to 36

25	5	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
26	6	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
27	6	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
28	6	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
29	6	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
30	6	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
31	7	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
32	7	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
33	7	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
34	7	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
35	7	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
36	8	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52

Daily Execution Plan - Days 37 to 48

37	8	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
38	8	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
39	8	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
40	8	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
41	9	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
42	9	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
43	9	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
44	9	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
45	9	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
46	10	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
47	10	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
48	10	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52

Daily Execution Plan - Days 49 to 60

49	10	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
50	10	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
51	11	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
52	11	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
53	11	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
54	11	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
55	11	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
56	12	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
57	12	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
58	12	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
59	12	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52
60	12	8.0	Production	Daily construction operations rhythm. Coordinate crews, check material levels, log site photos.	\$2,237.62	\$287.52

Commercial Risk Scenarios

Abnormal Ground	Rock or clay discovered requiring structural adjustments.	Geotechnical pre-inspections; provisional sums reserved in the contract.
Material Price Spikes	Cement or steel inflation erosion.	Lock supply agreements within 14 days of award. Reprice after quote expiry.
Cashflow Delay	Late client progress payments halts the site.	Certified payment milestones, retention bounds, mobilization deposits.

Procurement & Supply Chain Strategy

Bulk Materials	Order common bricks and cement weekly. Just-in-time storage.	Local flatbed truck transport.
Long-Lead Packages	Aluminium windows, roof trusses, kitchen cabinetry ordered week 4.	Direct fabricator dispatch with shop drawings freeze.

Resource & Crew Requirements Plan

Site Agent / PM	Full-time on site	Overall program and cost tracking, RFI setups.
Class 1 Bricklayers	Crews of 4 tradesmen	Lay masonry common clay bricks to target output.
General Helpers	Crews of 4 assistants	Material supply run, cement mixing, site housekeeping.

Health, Safety & QA/QC Checklists

Foundations Excavation	Bearing test compaction check.	Trench shoring, barrier tape setup.
Concrete Pours	Slump cylinder test, temperature records.	PPE safety boots, glove wear, hydration.
Masonry Walling	Plumb line alignment, joint size check.	Scaffolding levels guardrails verification.

Payment Milestones & Deliverables

1. Contract Mobilisation	10%	Design freeze register signed, insurance policy active.
2. Substructure Concrete Complete	20%	Strip foundations poured, ground slab cured, test cubes certified.
3. Superstructure Wallplate	30%	Superstructure brickwork laid, ring beams cast, structural checks signed.
4. Roof Shell & Dry-in	20%	Roof sheeting complete, aluminium window frames glazed, building sealed.
5. Practical Handover	20%	As-built manual delivered, occupation certificate, keys and snags closed.

Appendix - Data Summary

Total Cost Baseline	\$134,257.50
Target Gross Profit Margin	\$17,250.90
Contract Budget Ceiling	\$223,647.79
Weekly Plan Outlay Pages	2 Pages (Weeks 1 to 12)
Daily Workday Actions Pages	5 Pages (Days 1 to 60)
